

5th Street Bridge Update


Diana Langley

November 17, 2015


5th Street Bridge




Alignment

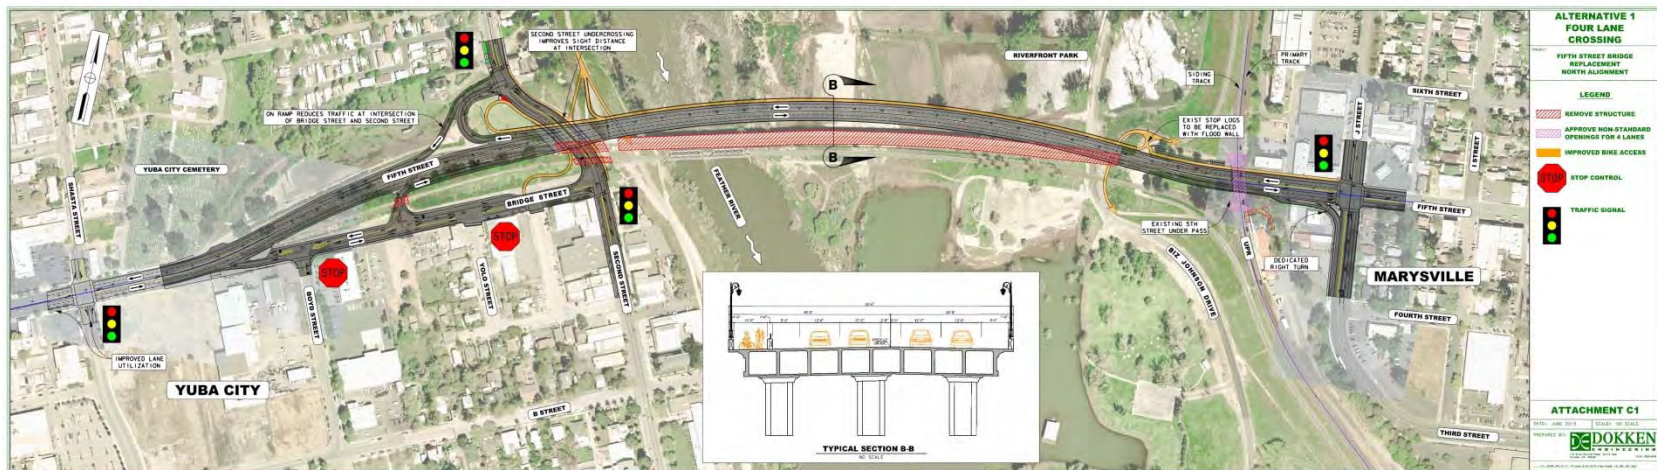

Typical Section

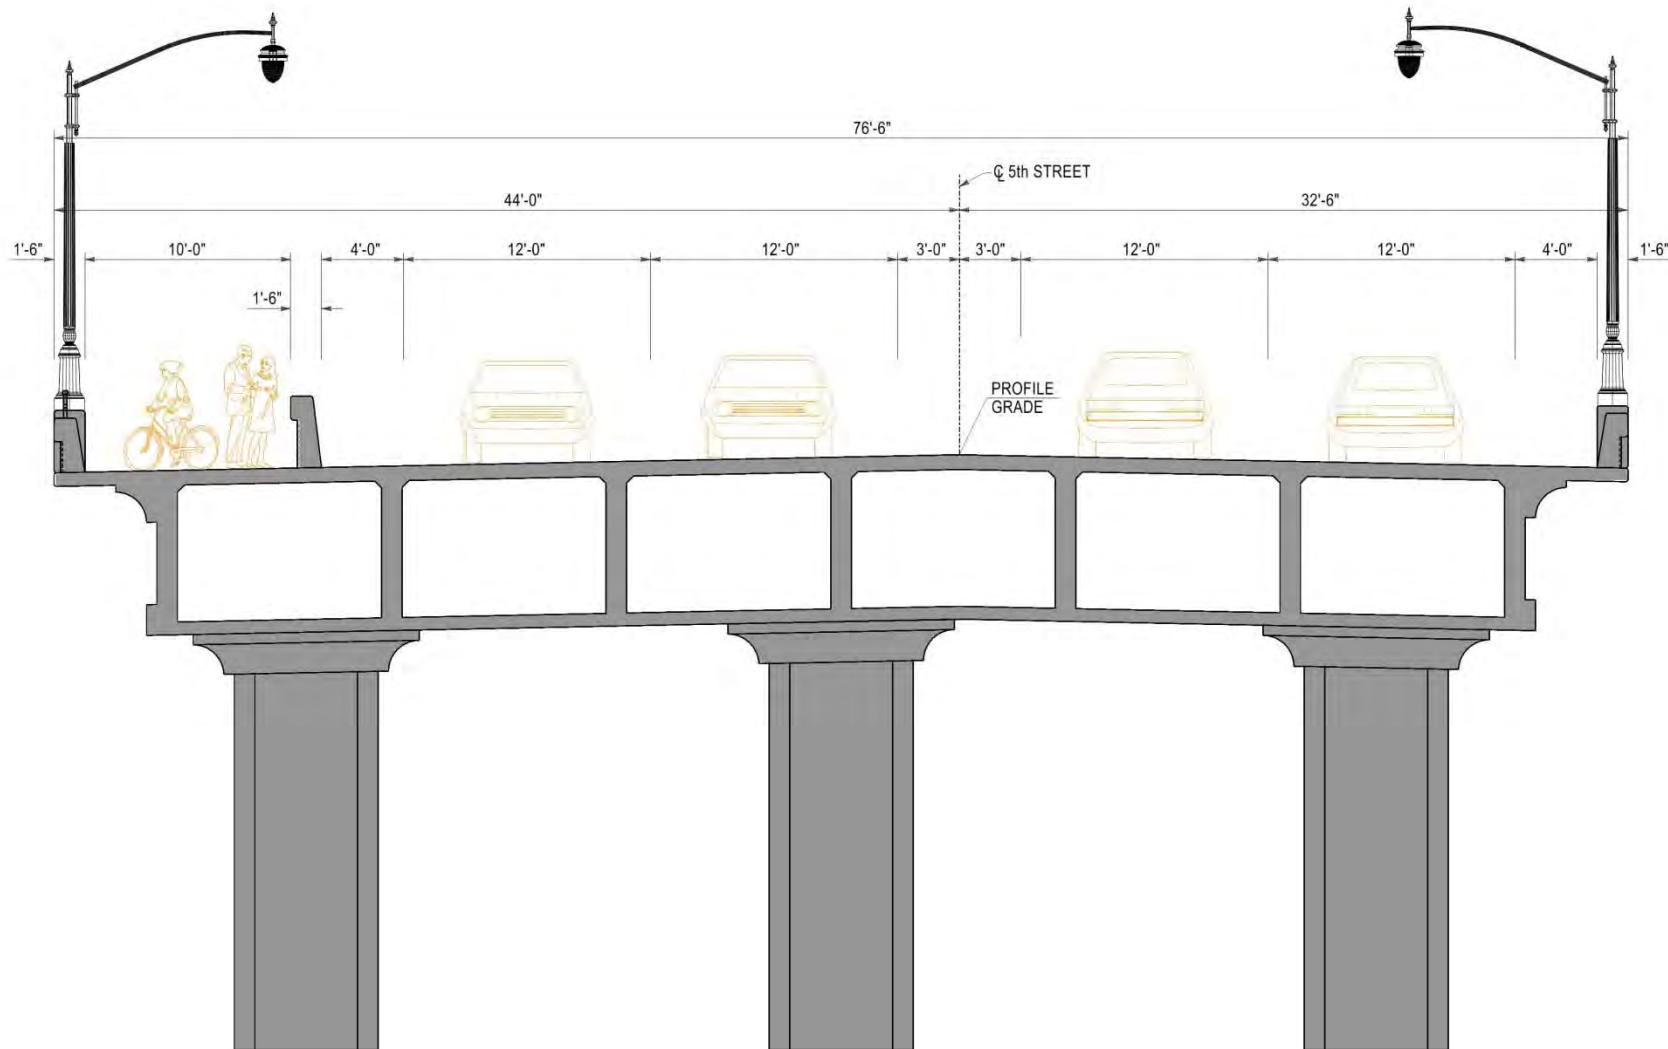


Alignment – Yuba City Side

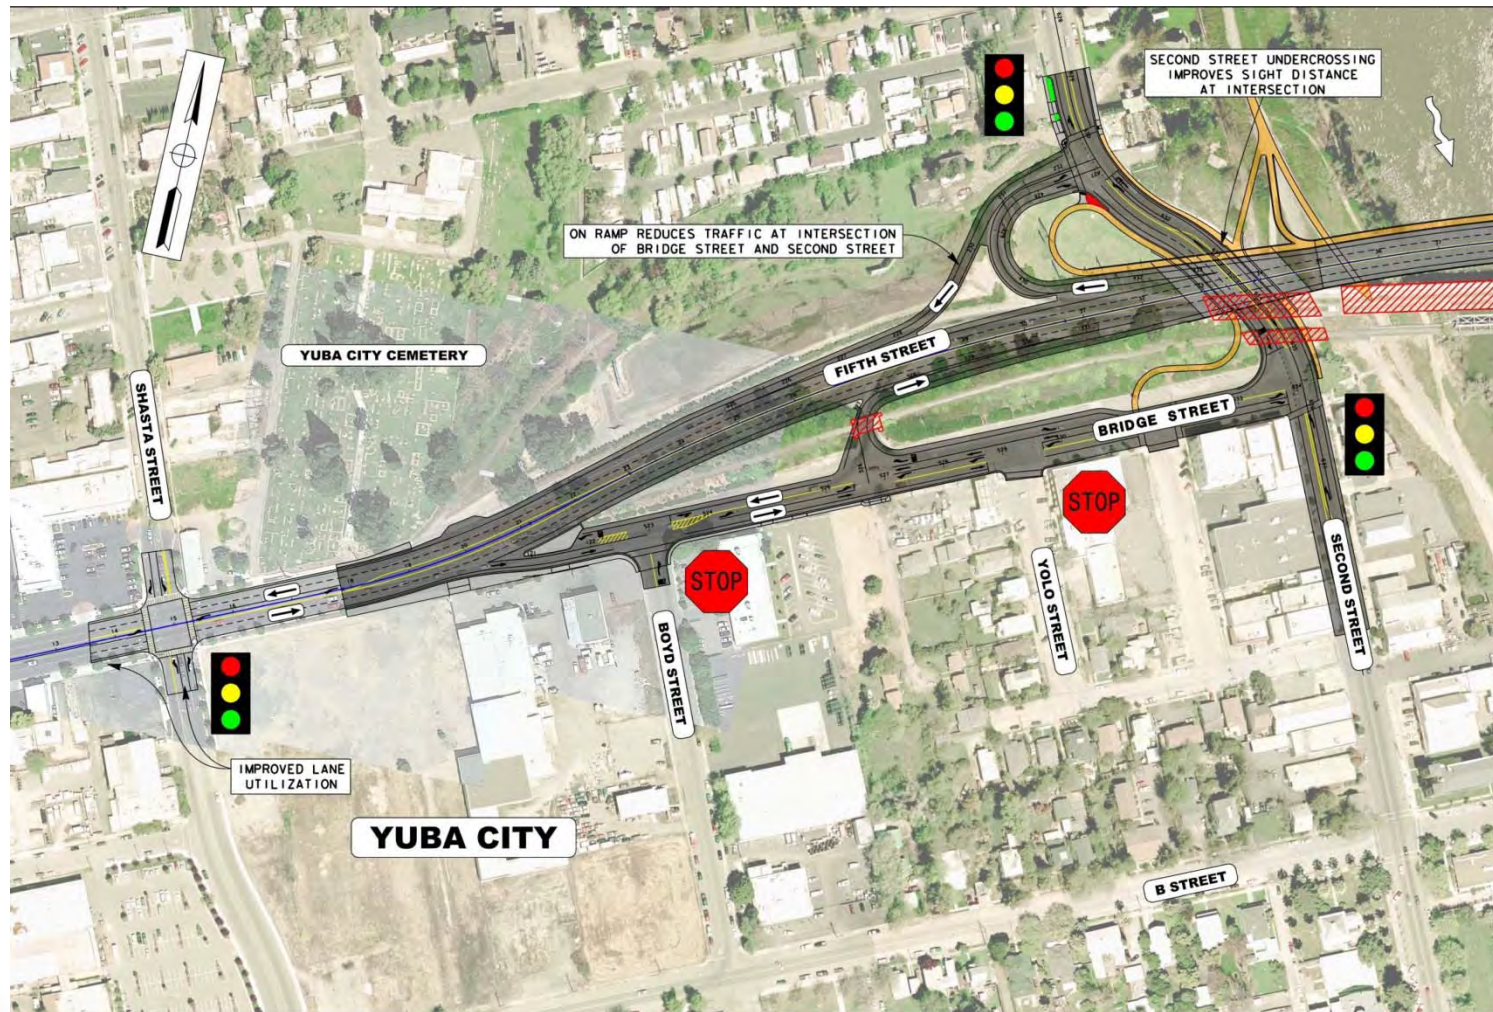

Alignment – Marysville Side



Alignment – Middle Section

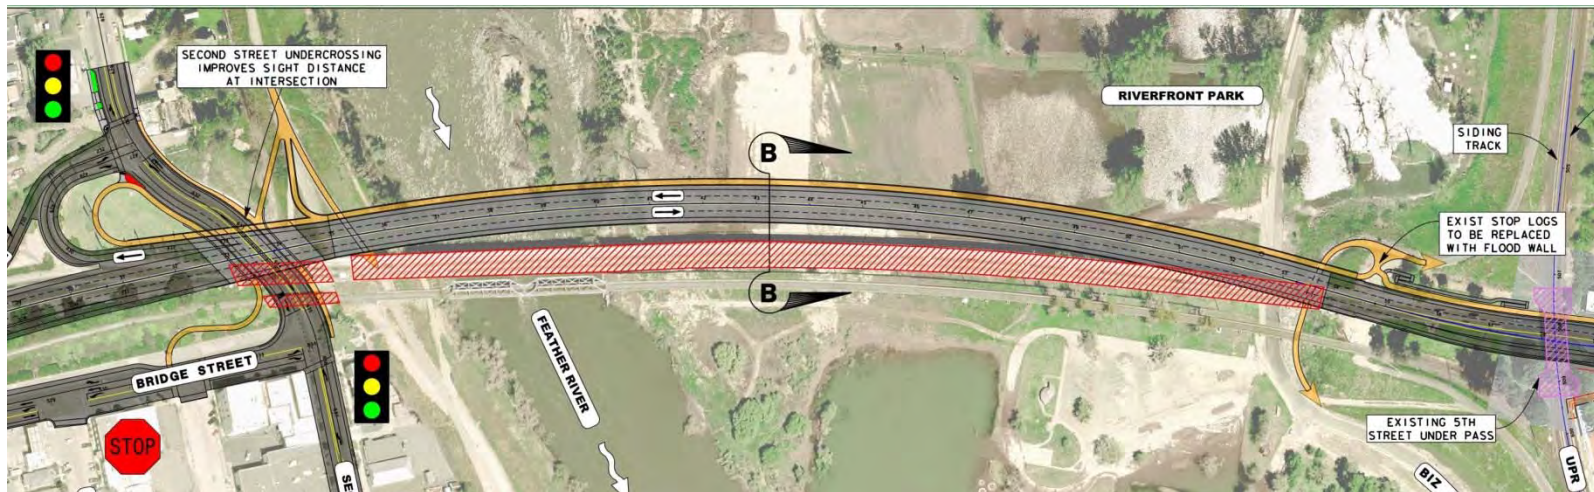

Completed to Date

- 9/15/10 – Contract Awarded for Preparation of Project Study Report/Project Report (PSR/PR)
- 4/8/13 – PSR/PR Completed
- 7/16/13 – Contract Awarded for Preliminary Design Services
- 12/12/13 – SACOG Awarded \$17.1 Million Grant
- 8/19/14 – City Council adopts Mitigated Negative Declaration and Awards Final Design Contract
- 8/27/14 – Caltrans Issues Finding of No Significant Impact
- 5/19/15 – Caltrans Authorizes the Final Design, Right-of-Way Acquisition, and Utility Relocation Portion of Project

Next Steps

- Meeting with Caltrans to discuss High Cost Project Agreement – January 2016
- Design Complete – November 2016
- Right-of-Way Certified – December 2016
- Construction
 - 2 Years to Complete
 - Currently anticipated to start July 2017 with completion in October 2019

Funding

- Project Estimate - \$70 Million
- Breakdown of Funding:

Funding Source	Amount
Highway Bridge Program	\$46,400,000
Regional Surface Transportation Program	\$3,200,000
Regional Improvement Program/State Transportation Improvement Program	\$17,400,000
Local Funds	\$2,600,000
Total:	\$69,600,000

*The PSR/PR phase was funded through the High Priority Projects program.

Questions?
